



Buckman Direct Diversion Board  
c/o Rick Carpenter, Project Manager  
Water Division, City of Santa Fe  
PO Box 909  
Santa Fe, NM 87504-0909

August 10, 2010

Dear Board Members,

Due to the unfortunate events associated with Tom Widner's passing, we were unable to provide the BDD a complete preliminary draft report of the Buckman Direct Diversion Project Independent Peer Review by the May, 2010 date initially set within our proposal. Dr. Brent Finley at ChemRisk has assumed the role as principal investigator for the independent peer review, and is coming up to speed with the current incomplete version of the preliminary draft report.

We are confident that we can provide a complete preliminary draft report in accordance with the amended schedule. Please feel free to contact Dr. Finley or myself with any questions.

Regards,

A handwritten signature in black ink, appearing to read "Matthew H. Le".

Matthew H. Le, M.P.H.  
Associate Health Scientist


**ChemRisk**

25 Jessie Street at Ecker Square, Suite 1800

San Francisco, CA 94105

[www.chemrisk.com](http://www.chemrisk.com)

# Schedule Graphic, Independent Peer Review Project as Amended August 10th, 2010

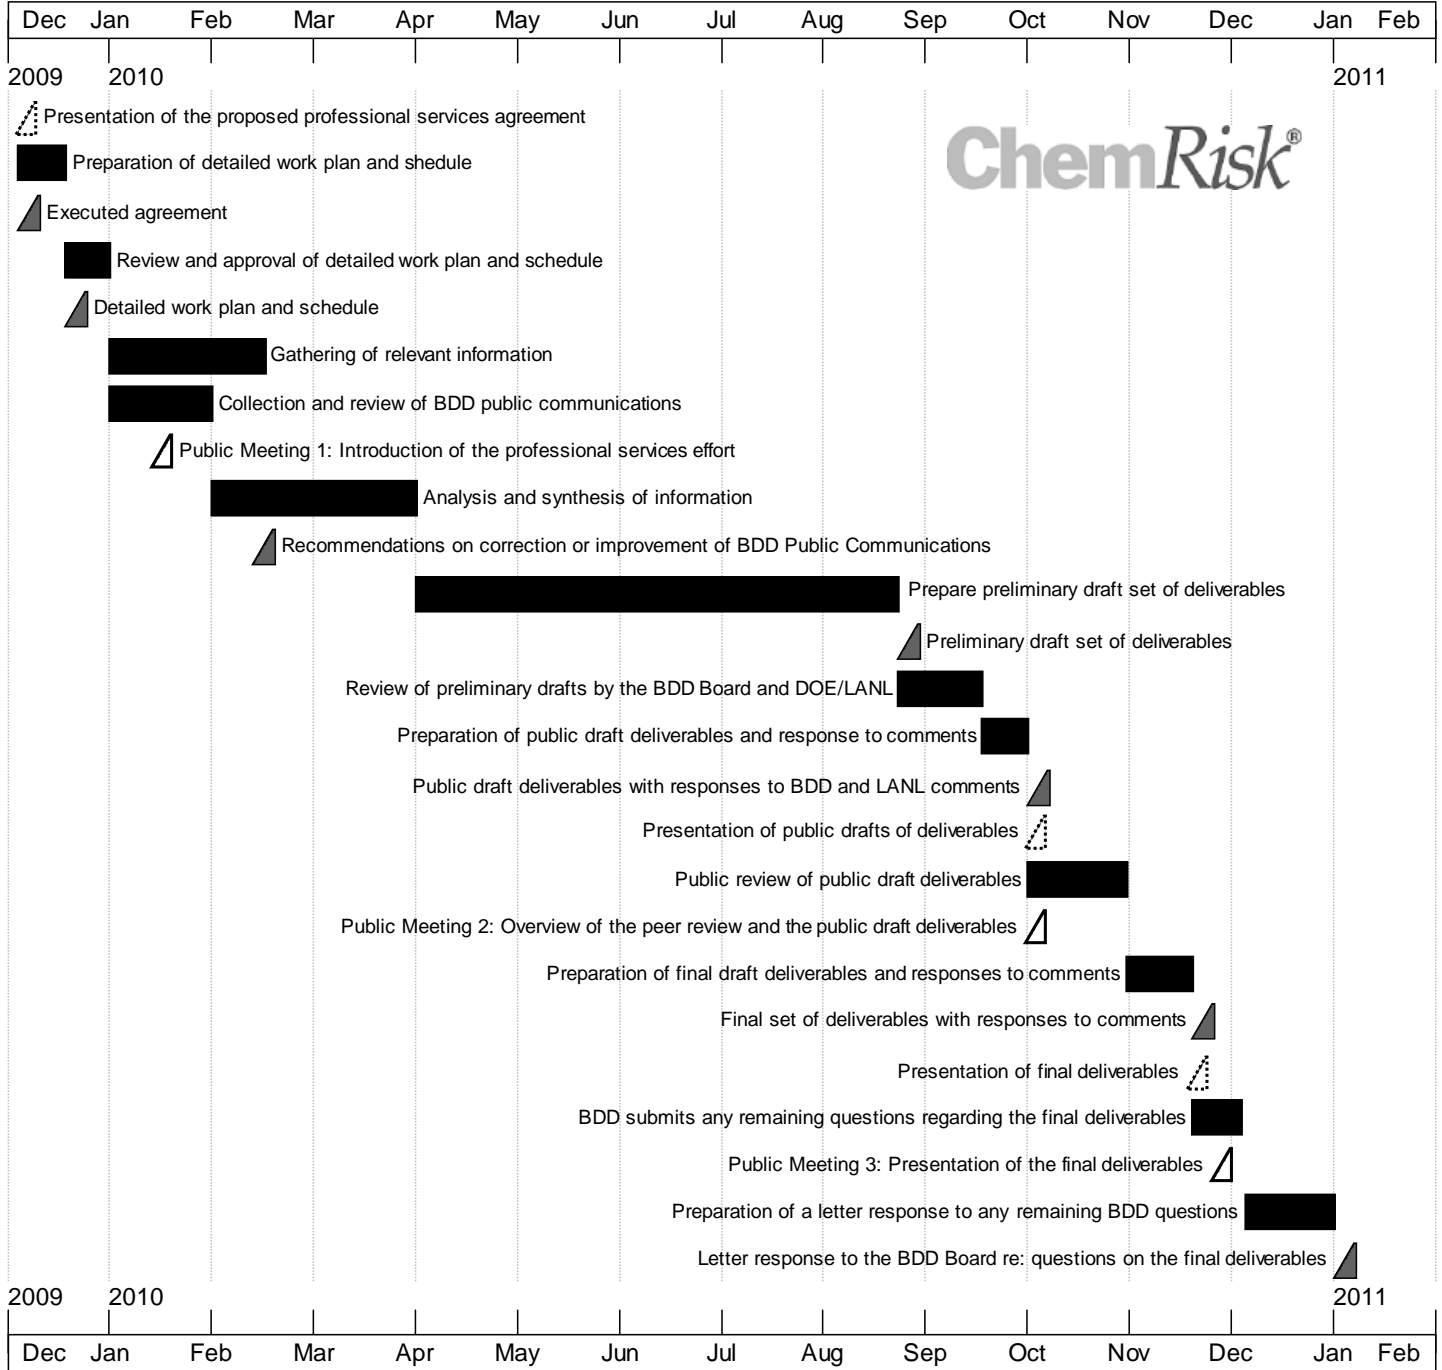

Legend:

■ Information Gathering, Analysis, and Reporting

■ Milestones and Deliverables

□ Peer Review Team Presentations to the BDD Board

□ Public Meetings of the Independent Peer Review Project

<b>Event Name</b>	<b>Start Date</b>	<b>End Date</b>	<b>Category</b>
Preparation of detailed work plan and shedule	Dec 04 2009	Dec 18 2009	Information Gathering, Analysis, and Reporting
Review and approval of detailed work plan and schedule	Dec 18 2009	Dec 31 2009	Information Gathering, Analysis, and Reporting
Collection and review of BDD public communications	Jan 01 2010	Jan 31 2010	Information Gathering, Analysis, and Reporting
Gathering of relevant information	Jan 01 2010	Feb 15 2010	Information Gathering, Analysis, and Reporting
Analysis and synthesis of information	Feb 01 2010	Apr 01 2010	Information Gathering, Analysis, and Reporting
Preparation of preliminary draft deliverables	Apr 01 2010	Aug 23 2010	Information Gathering, Analysis, and Reporting
Review of preliminary drafts by the BDD Board and DOE/LANL	Aug 23 2010	Sep 17 2010	Information Gathering, Analysis, and Reporting
Preparation of public draft deliverables and response to comments	Sep 17 2010	Sep 30 2010	Information Gathering, Analysis, and Reporting
Public review of public draft deliverables	Oct 01 2010	Oct 30 2010	Information Gathering, Analysis, and Reporting
Preparation of final draft deliverables and responses to comments	Oct 30 2010	Nov 19 2010	Information Gathering, Analysis, and Reporting
BDD submits any remaining questions regarding the final deliverables	Nov 19 2010	Dec 04 2010	Information Gathering, Analysis, and Reporting
Preparation of a letter response to any remaining BDD questions	Dec 05 2010	Dec 31 2010	Information Gathering, Analysis, and Reporting
Executed agreement	Dec 04 2009		Milestones and Deliverables
Detailed work plan and schedule	Dec 18 2009		Milestones and Deliverables
Recommendations on correction or improvement of BDD Public Communications	Feb 12 2010		Milestones and Deliverables
Preliminary draft set of deliverables	Aug 23 2010		Milestones and Deliverables
Public draft deliverables with responses to BDD and LANL comments	Sep 30 2010		Milestones and Deliverables

Final set of deliverables with responses to comments	Nov 19 2010	Milestones and Deliverables
Letter response to the BDD Board re: questions on the final deliverables	Dec 31 2010	Milestones and Deliverables
Presentation of the proposed professional services agreement	Dec 03 2009	Peer Review Team Presentations to the BDD Board
Presentation of public drafts of deliverables	Sep 29 2010	Peer Review Team Presentations to the BDD Board
Presentation of final deliverables	Nov 17 2010	Peer Review Team Presentations to the BDD Board
Public Meeting 1: Introduction of the professional services effort	Jan 13 2010	Public Meetings of the Independent Peer Review Project
Public Meeting 2: Overview of the peer review and the public draft deliverables	Sep 29 2010	Public Meetings of the Independent Peer Review Project
Public Meeting 3: Presentation of the final deliverables	Nov 24 2010	Public Meetings of the Independent Peer Review Project
